

DOWNES ELEMENTARY SCHOOL RENOVATION & EXPANSION

Board Presentation – Construction Documents January 11, 2022





Agenda

- Scope Parameters & Program Goals
- The New Learning Environment
- Construction DocumentBudget Review
- Next Steps





Scope Parameters & Program Goals



Scope Parameters & Program Goals


- 4 New Classrooms
- 2-Storey Addition
- Planned to accommodate the Chinese Immersion Program








The New Learning Environment

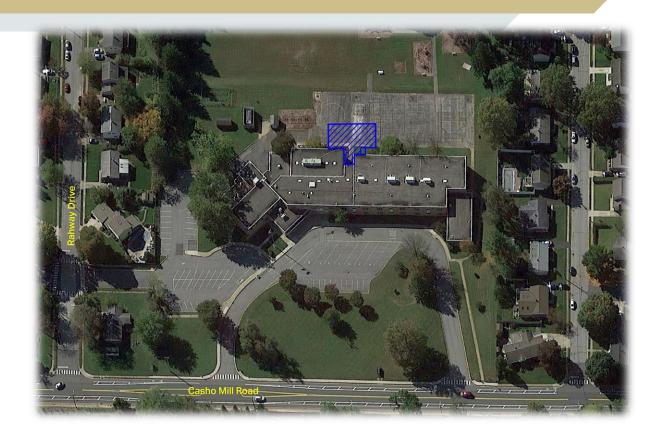

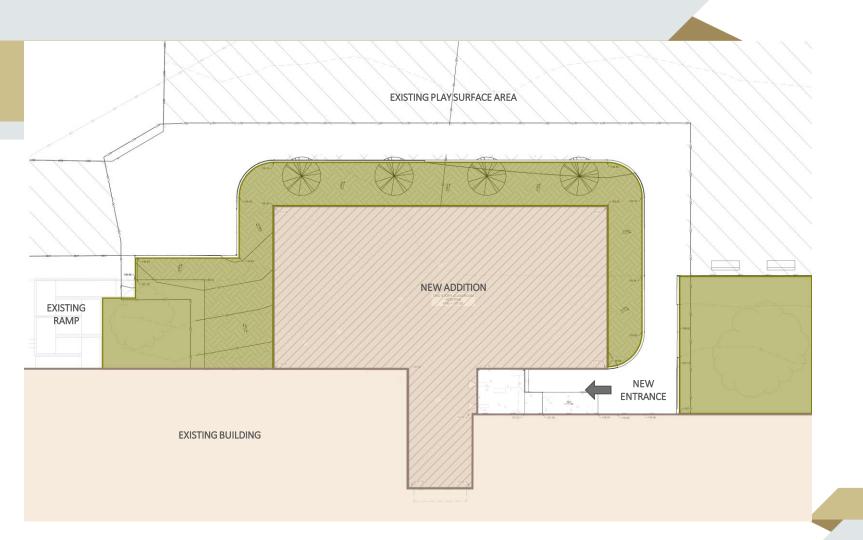






The New Learning Environment


Partial First Floor Plan

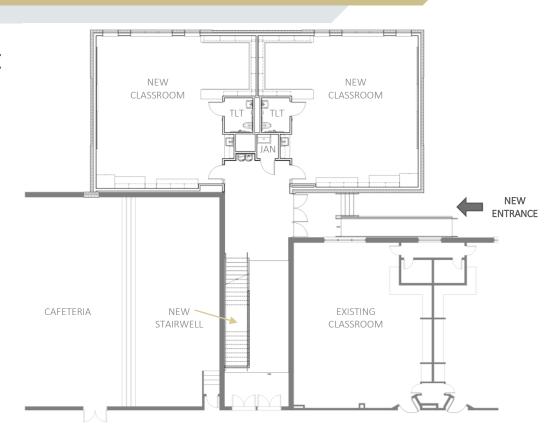



The New Learning Environment

Partial Second Floor Plan

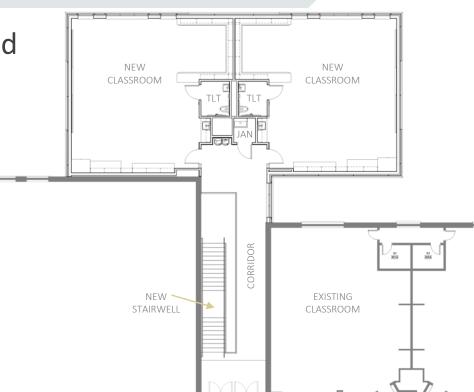





Schematic Design Budget Review

- Project Budget
- Construction Document Estimate
 - Base Bid: 4 Classroom Addition
 - Alt 1: Addition HVAC
 - Alt 2: Addition Flooring
 - Alt 3: Re-pave Rear Play Area

\$2,239,000

\$2,816,020

Shortfall \$577,022

- \$2,382,364
 - \$208,271
 - \$36,251
 - \$111,420





Next Steps

- Board Review & Approval of CD Documentation (January)
- Submit CD Documentation to DDOE
- Obtain Final Approvals from DOE & DFM (January)
- Project Bidding (February) & Award (March)
- Construction Start (June 2022)
- Substantial Completion (August 2023)

Thank You

